



SFFD AMBULANCE DEPLOYMENT FACILITY

June 2020 Construction Update by ADC Dawn DeWitt



AMBULANCE DEPLOYMENT FACILITY

Overview



ADF Update—ADC DeWitt

- ❖ Background
- ❖ Budget
- ❖ Schedule
- ❖ Photo Walk-Through

EMS Division Update—ADC Tong



AMBULANCE DEPLOYMENT FACILITY

Background



- 2016 Public Health and Safety Bond
- Budget \$48,600,000
- Construct a modern, seismically safe EMS building
 - ❖ Replaces Current Station 49 on Evans Street



AMBULANCE DEPLOYMENT FACILITY Budget



	Amount	Percentage
Budget	\$48,600,000	100%
Financing	(\$719,591)	1.5%
FF&E Reduction by BOS (2019)	(\$137,511)	2.8%
Operating Budget	\$47,742,898	98.2%
Available Balance	\$8,352,644	17.2%

Project is On Budget!!



AMBULANCE DEPLOYMENT FACILITY


Schedule



Notice to Proceed
10/22/2018

Substantial Completion
7/22/2020

Revised Substantial Completion
10/26/2020

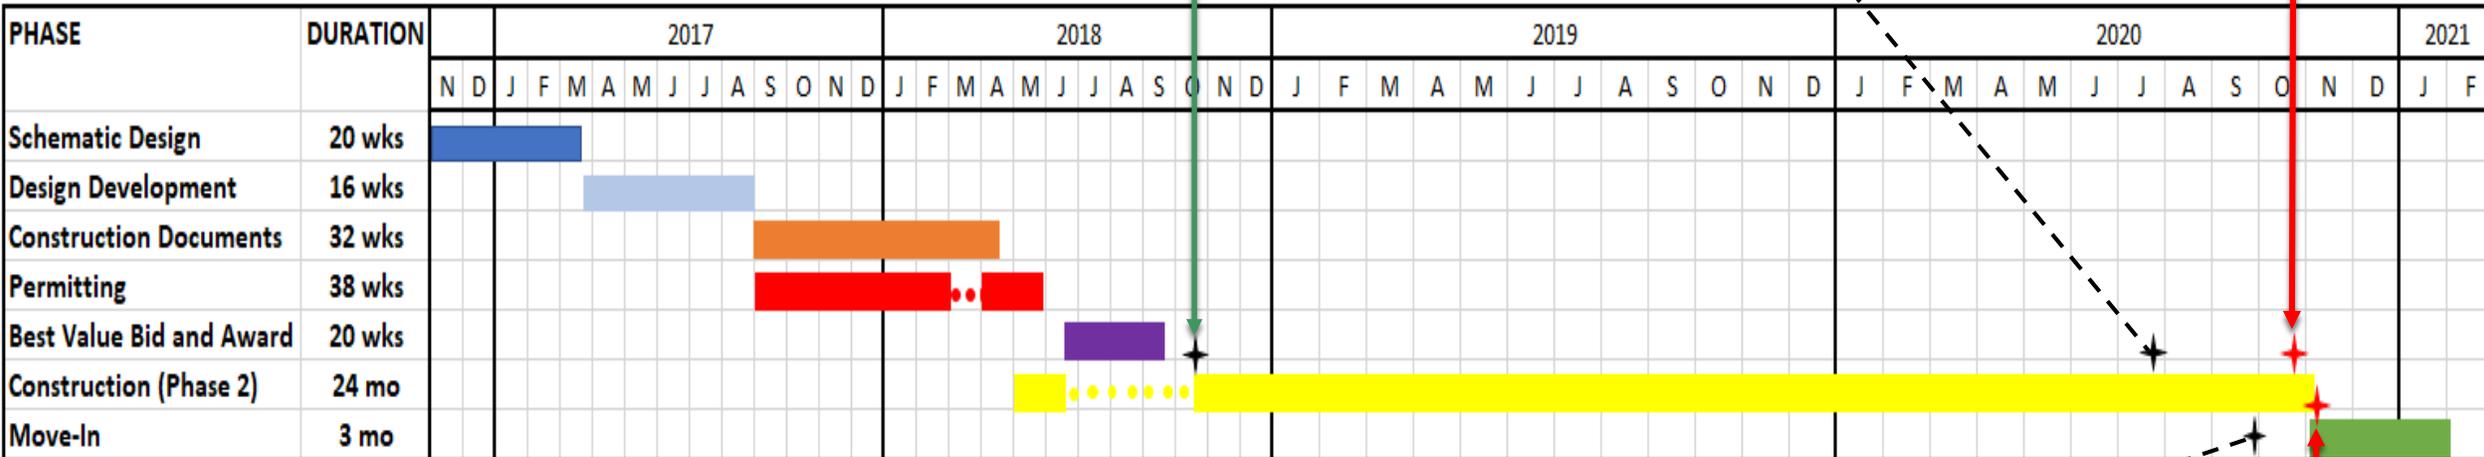

Projected 55- to 57-day Delay

Final Completion
9/28/2020

Revised Final Completion
11/09/2020



AMBULANCE DEPLOYMENT FACILITY

Artist Renderings of Exterior



View from Jerrold




View from McKinnon



AMBULANCE DEPLOYMENT FACILITY

Construction Progress—View from Jerrold Street




Erection of Steel Canopy - September 30, 2019






AMBULANCE DEPLOYMENT FACILITY

Construction Progress—Yard Underground Fuel Tanks

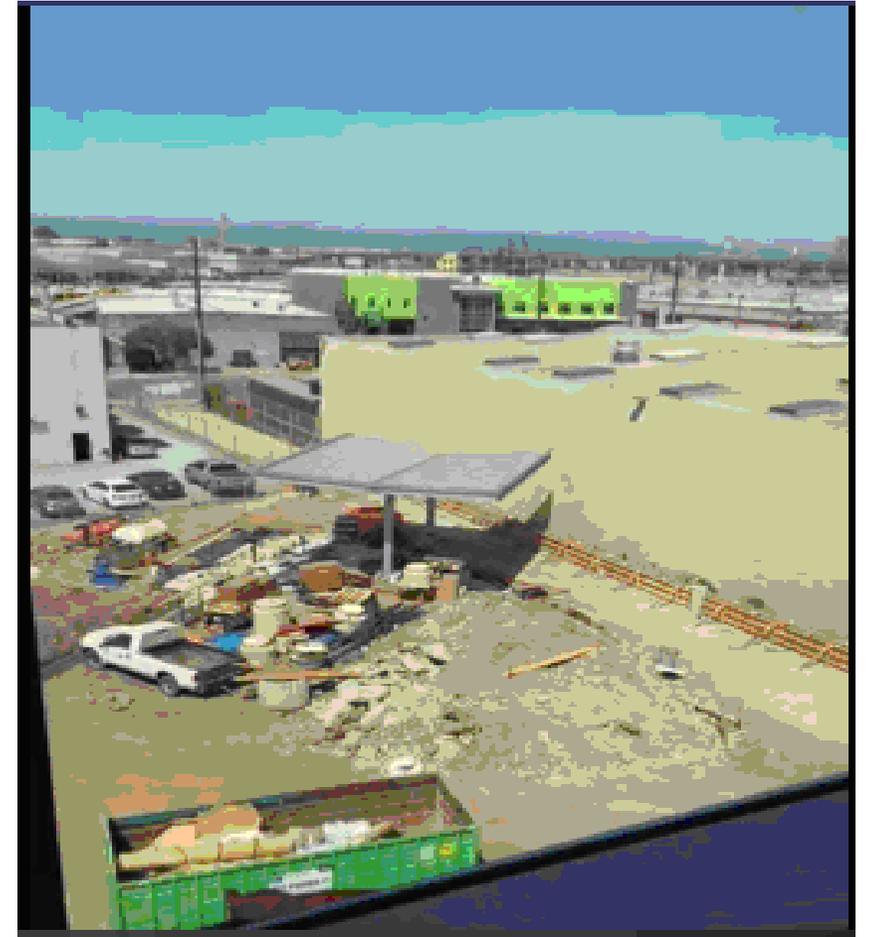



AMBULANCE DEPLOYMENT FACILITY Construction Progress—Parking Structure



Installing Stair Handrails at Ambulance Parking Garage (March 31, 2020)




All Hands on Deck! Concrete Placed at Parking Garage - October 25, 2019



AMBULANCE DEPLOYMENT FACILITY

Construction Progress—1st Floor






Warehouse with view of 2nd Floor Catwalk



AMBULANCE DEPLOYMENT FACILITY

Construction Progress—1st Floor

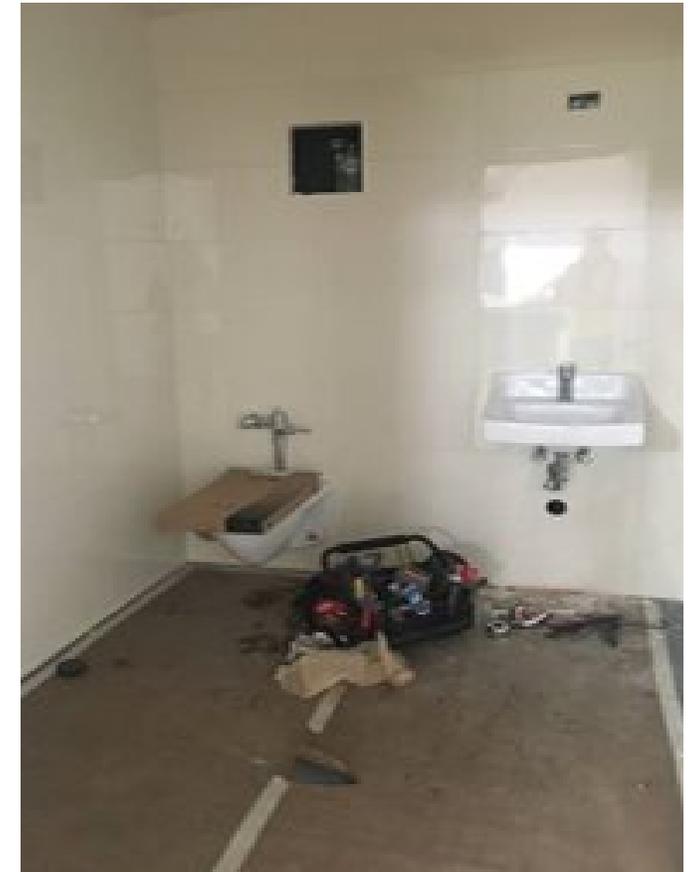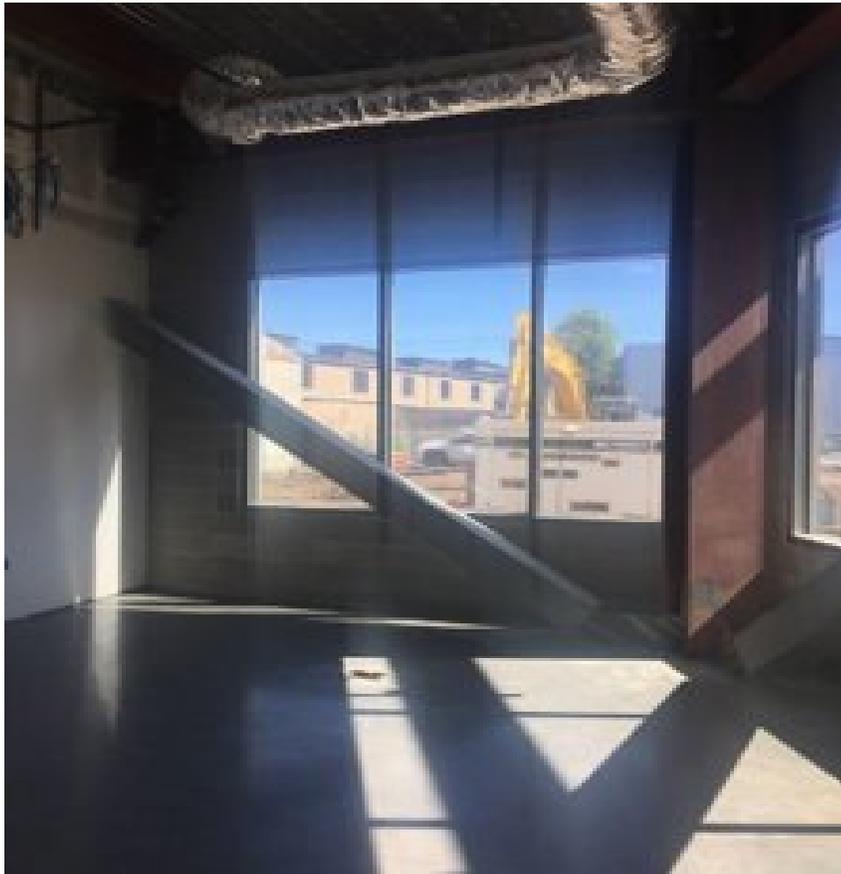


RC Room, Mechanical and IT Room, 1st Floor Restroom



AMBULANCE DEPLOYMENT FACILITY

Construction Progress—2nd Floor



View of Warehouse from EMS I's Office




View of RC's Office from 2nd Floor Catwalk



AMBULANCE DEPLOYMENT FACILITY


Construction Progress—2nd Floor

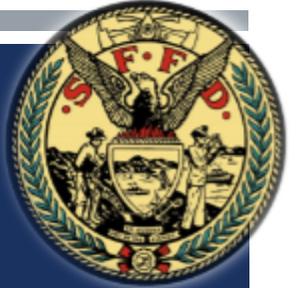

Biomedical (Controlled Substances) Room



Eye Wash Station

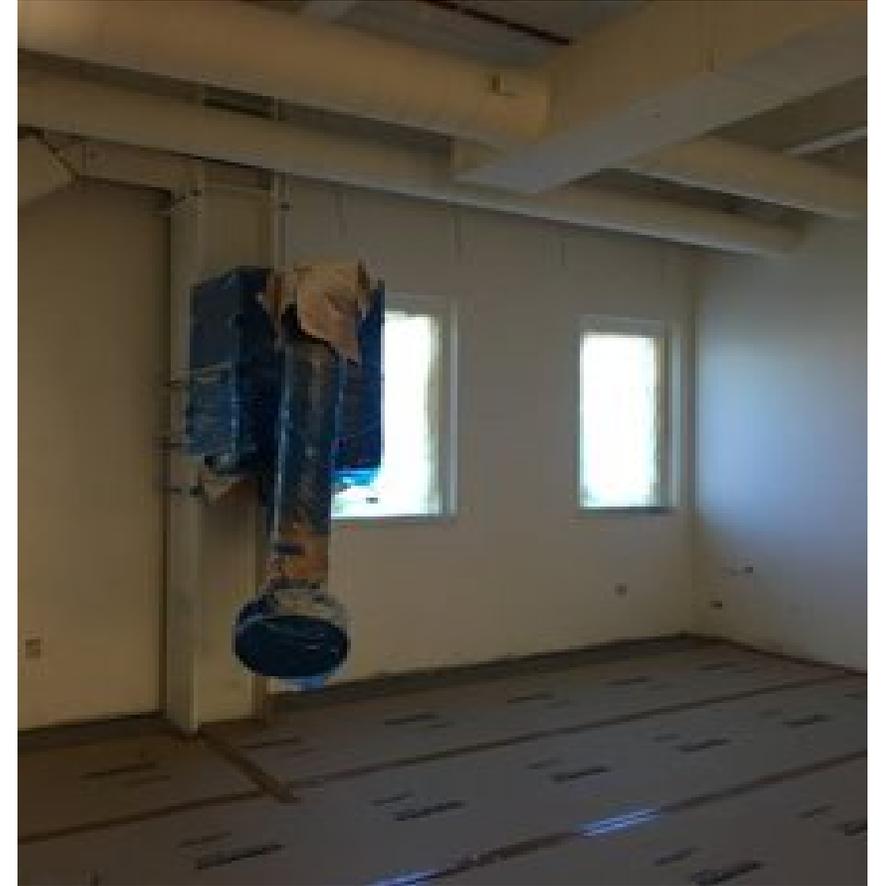


Gurney Repair Room



AMBULANCE DEPLOYMENT FACILITY

Construction Progress—3rd Floor




Break Room and Kitchen Area



AMBULANCE DEPLOYMENT FACILITY

Construction Progress—3rd Floor

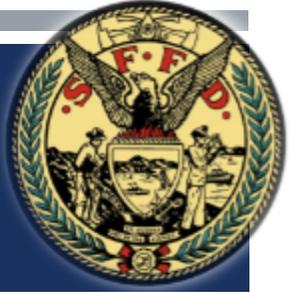

Corridor adjacent to Gym




Locker Rooms



AMBULANCE DEPLOYMENT FACILITY

Construction Progress—4th Floor

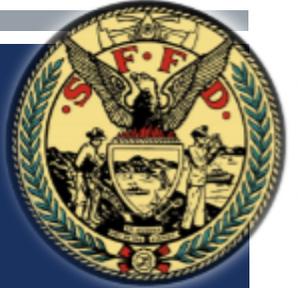

Conference Room





Open Office and Offices



AMBULANCE DEPLOYMENT FACILITY

Entrance Gate from Jerrold



Artist: Michael Bartalos



AMBULANCE DEPLOYMENT FACILITY

Exit Gate to McKinnon

